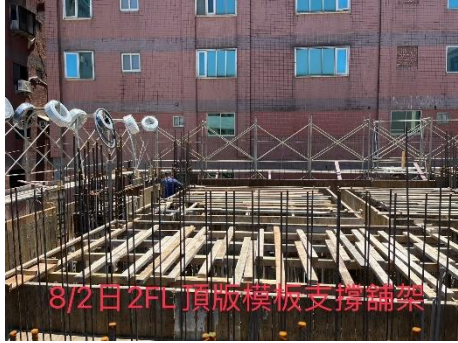


恂品里山

No	日期	工程項目	施工位置及內容說明
1	113/08/01~113/08/31	結構工程	1. 2F 頂版梁模組架 2. 2F 頂版模板支撐鋪架
 			
2	113/08/01~113/08/31	結構工程	1. 2F 頂版水電配管 2. 2F 頂版模板固結
 			

恂品里山

No	日期	工程項目	施工位置及內容說明
3	113/08/01~113/08/31	結構工程	1. 2F 頂版 RC 澆灌檢測 2. 2F 頂版澆築水電顧管
 8/10日2FL頂版RC澆築檢測  8/10日2FL頂版澆築水電顧管			
4	113/08/01~113/08/31	結構工程	1. 2F 頂版澆築整體粉光 2. 3F 鷹架搭架
 8/10日2FL頂版澆築整體粉光  8/12日3FL鷹架搭架			

恂品里山

No	日期	工程項目	施工位置及內容說明
5	113/08/01~113/08/31	結構工程	1. 3F 柱筋綁紮 2. 3F 柱筋組立完成
 			
6	113/08/01~113/08/31	結構工程	1. 3F 模板單面模組立 2. 3F 水電放置箱體及配管
 			

恂品里山

No	日期	工程項目	施工位置及內容說明
7	113/08/01~113/08/31	結構工程	1. 3F 牆筋綁紮 2. 3F 牆面水電配管
 			
8	113/08/01~113/08/31	結構工程	1. 3F 牆面模板封模 2. 3F 頂版梁側模板架鋪
 			

恂品里山

No	日期	工程項目	施工位置及內容說明
9	113/08/01~113/08/31	結構工程	1. 3F 頂版模板架鋪 2. 3F 頂版模板收尾
 			
10	113/08/01~113/08/31	結構工程	1. 3F 頂版梁筋綁紮 2. 3F 頂版水電配管完成
 			
