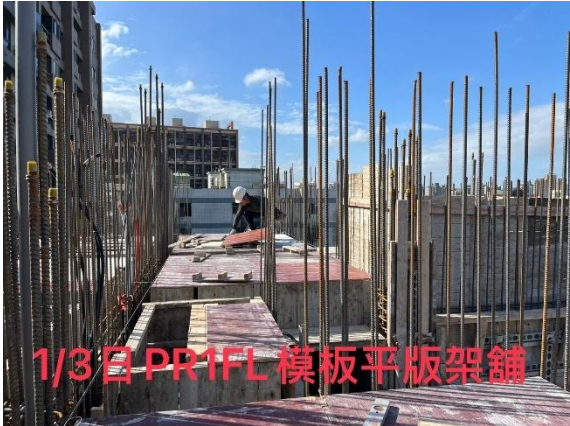


恂品里山

No	日期	工程項目	施工位置及內容說明
1	114/01/01~114/01/24	結構工程	1. PR1F 模板封模 2. 4F 室內砌磚隔間
  1/1日 PR1FL 模板封模 1/1日 4FL 室內砌磚隔間			
2	114/01/01~114/01/24	結構工程	1. PR1F 模板女兒牆封模 2. PR1F 女兒牆水電配管
  1/2日 PR1FL 模板女兒牆封模 1/2日 PR1FL 女兒牆水電配管			

恂品里山

No	日期	工程項目	施工位置及內容說明
3	114/01/01~114/01/24	結構工程	1. PR1F 模板平版架鋪 2. PR1F 模板板面架鋪
 			
4	114/01/01~114/01/24	結構工程	1. PR1F 模板女兒牆封模固定 2. PR1F 模板完成現場
 			

恂品里山

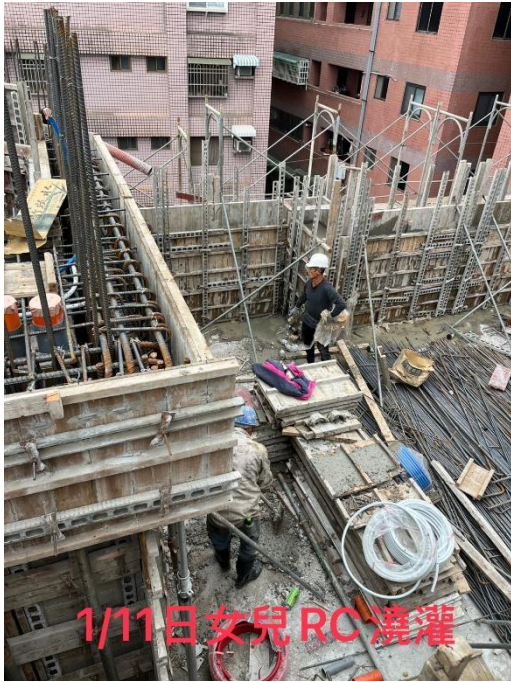
No	日期	工程項目	施工位置及內容說明
5	114/01/01~114/01/24	結構工程	1. PR1F 頂版鋼筋綁紮 2. PR1F 頂版水電配管
 			
6	114/01/01~114/01/24	結構工程	1. PR1F 頂版梁筋綁紮 2. PR1F 柱筋鋼筋綁紮
 			

忸品里山

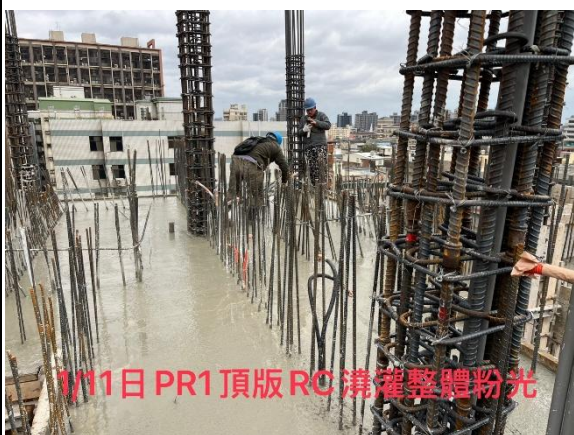
No	日期	工程項目	施工位置及內容說明
7	114/01/01~114/01/24	結構工程	1. PR1F 柱筋 2. 5F 室內砌磚隔間
 			
8	114/01/01~114/01/24	結構工程	1. 屋頂女兒牆模板組立完成 2. PR1F 頂版 RC 澆灌
 			

恂品里山

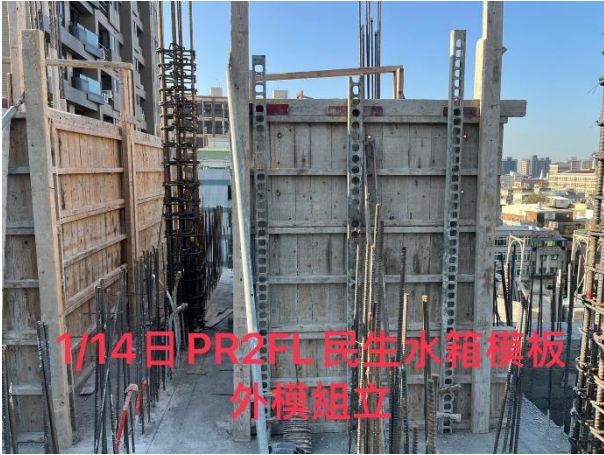
No	日期	工程項目	施工位置及內容說明
9	114/01/01~114/01/24	結構工程	1. PR1F 女兒牆 RC 澆灌 2. PR1F 樓梯 RC 澆灌完成



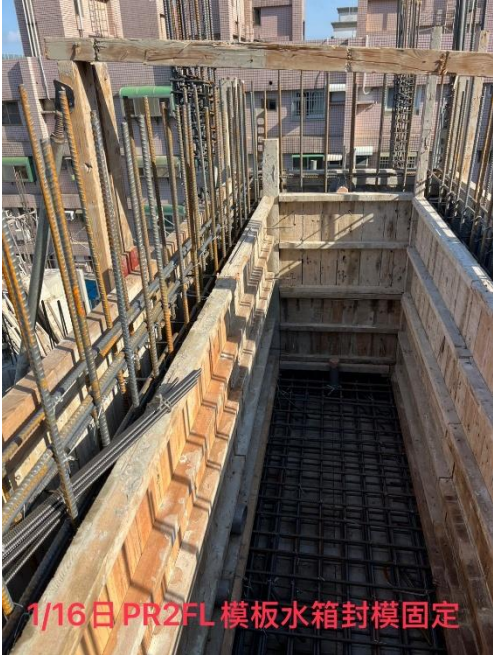
10	114/01/01~114/01/24	結構工程	1. PR1F 頂版 RC 澆灌整體粉光 2. PR2F 放樣
----	---------------------	------	------------------------------------



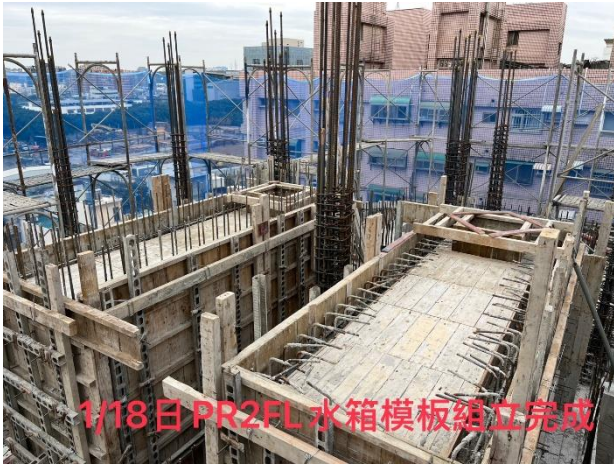
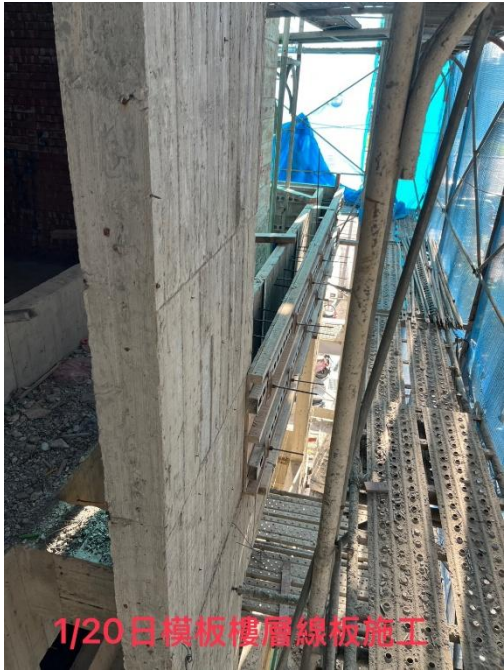
恂品里山

No	日期	工程項目	施工位置及內容說明
11	114/01/01~114/01/24	結構工程	1. PR2F 民生水箱模板外模組立 2. PR2F 水箱底層及牆壁鋼筋綁紮
 1/14日 PR2FL 民生水箱模板外模組立  1/16日 PR2FL 水箱底層及牆壁鋼筋綁紮			
12	114/01/01~114/01/24	結構工程	1. PR2F 水箱水電配管 2. PR2F 模板水箱組模
 1/16日 PR2FL 水箱水電配管  1/16日 PR2FL 模板水箱組模			

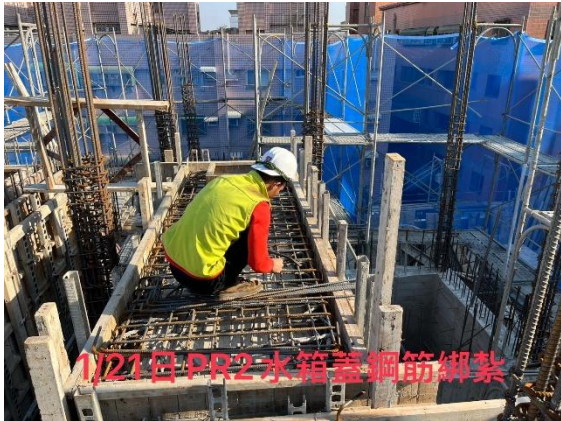
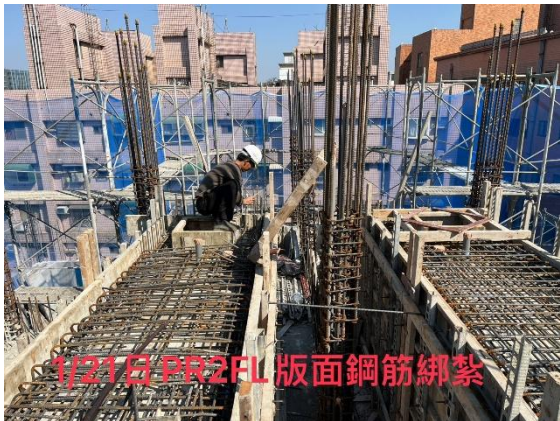
恂品里山

No	日期	工程項目	施工位置及內容說明
13	114/01/01~114/01/24	結構工程	1. 泥作外牆吊線 2. PR2F 模板水箱封模固定
 			
14	114/01/01~114/01/24	結構工程	1. PR2F 水箱底灌漿 2. PR2F 水箱底/側牆灌漿完成
 			

忸品里山

No	日期	工程項目	施工位置及內容說明
15	114/01/01~114/01/24	結構工程	1. PR2F 水箱模板組立完成 2. 模板樓層線板施工
 1/18日PR2FL水箱模板組立完成  1/20日模板樓層線板施工			
16	114/01/01~114/01/24	結構工程	1. PR2F 水箱水電放置套管 2. 6F 水電管道間管路配置
 1/20日PR2FL水箱水電放置套管  1/20日6FL水電管道間管路配置			

恂品里山

No	日期	工程項目	施工位置及內容說明
17	114/01/01~114/01/24	結構工程	1. PR2F 水箱蓋鋼筋綁紮 2. PR2F 版面鋼筋綁紮
 			
18	114/01/01~114/01/24	結構工程	1. PR2F 水箱頂板 RC 灌漿振動棒施工 2. PR2F 模板拆除水箱外模
