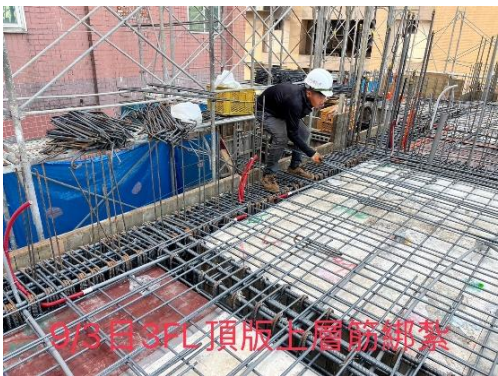


恂品里山

No	日期	工程項目	施工位置及內容說明
1	113/09/01~113/09/30	結構工程	1. 3F 頂版下層筋綁紮 2. 3F 頂版模板固結
 			
2	113/09/01~113/09/30	結構工程	1. 3F 頂版水電配管 2. 3F 頂版上層筋綁紮
 			

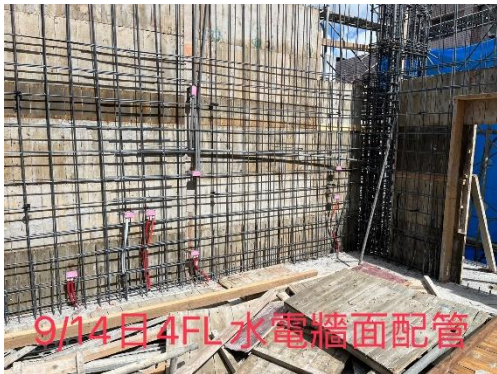
恂品里山

No	日期	工程項目	施工位置及內容說明
3	113/09/01~113/09/30	結構工程	1. 3F 頂版鋼筋預留筋綁紮 2. 3F 頂版 RC 澆築
 			
4	113/09/01~113/09/30	結構工程	1. 3F 頂版 RC 澆築振動及整平 2. 3F 模板拆除外模
 			

恂品里山

No	日期	工程項目	施工位置及內容說明
5	113/09/01~113/09/30	結構工程	1. 4F 放樣標示柱牆位置 2. 4F 鷹架搭設外架
 9/6日4FL 放樣標示柱牆位置  9/7日4FL 鷹架搭設外架			
6	113/09/01~113/09/30	結構工程	1. 4F 柱筋綁紮 2. 4F 模板單面模組立
 9/9日4FL 柱筋綁紮  9/10日4FL 模板單面模組立			

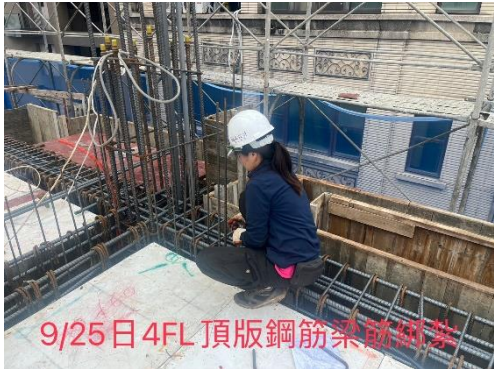
恂品里山

No	日期	工程項目	施工位置及內容說明
7	113/09/01~113/09/30	結構工程	1. 4F 牆面鋼筋綁紮 2. 4F 水電牆面配管
 9/13日4FL 牆面鋼筋綁紮  9/14日4FL 水電牆面配管			
8	113/09/01~113/09/30	結構工程	1. 4F 牆面模板封膜 2. 4F 牆面模板固定
 9/16日4FL 牆面模板封模  9/18日4FL 牆面模板固定			

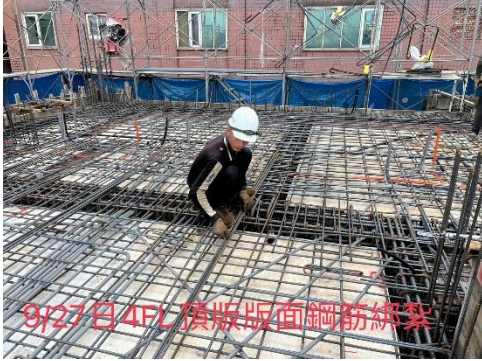
恂品里山

No	日期	工程項目	施工位置及內容說明
9	113/09/01~113/09/30	結構工程	1. 4F 頂版組梁 2. 4F 頂版梁底模板架鋪
 			
10	113/09/01~113/09/30	結構工程	1. 4F 頂版模板支撐架鋪 2. 4F 頂版模板組立
 			

恂品里山

No	日期	工程項目	施工位置及內容說明
11	113/09/01~113/09/30	結構工程	1. 4F 頂版梁筋綁紮 2. 4F 頂版水電配管
 			
12	113/09/01~113/09/30	結構工程	1. 4F 頂版鋼筋梁筋綁紮 2. 4F 模板樓梯施工
 			

恂品里山

No	日期	工程項目	施工位置及內容說明
13	113/09/01~113/09/30	結構工程	1. 4F 頂版模板外膜固定 2. 4F 頂版版面鋼筋綁紮
 			
14	113/09/01~113/09/30	結構工程	1. 4F 頂版技師查驗 2. 4F 頂版建築師查驗
 			

恂品里山

No	日期	工程項目	施工位置及內容說明
15	113/09/01~113/09/30	結構工程	1. 4F 頂版水電巡查收尾 2. 鷹架帆布整理預防颱風措施
 			
16	113/09/01~113/09/30	結構工程	1. 4F 頂版模板加強防範颱風 2. 4F 頂版雜工雜物清理
 
